

# Annexure C

## PROFORMA FOR SAFE DRINKING WATER AND SANITARY CONDITION CERTIFICATE

No. 2852874/2025

Dated: 11/07/2025

It is certified that an inspection team headed by Wilson M. X Clean City Manager

(Name of Officers with designation) from Piravom Municipality PHED

inspected the Vivekananda Public School, Piravom

(Name & Address of the school) on 03/07/2025 (date of inspection) and on the basis of

Water Test Report (Attached) bearing no. KWA/QCSDL/PVM/2133-25-26 dated 01/07/2025

of Quality Control Sub District Lab Piravom (PHED Lab) certified that the


Vivekananda Public School (Name of school) has safe drinking water

facilities for the students and members of staff of the institution. School is also maintains the hygienic sanitation condition in the school building & the campus as per norms prescribed by the Central/ State/ U.T. Govt.

This certificate is valid till 10/07/2026

Signature with Seal: Wilson M. X  
Name: Wilson M. X  
Designation: Clean City Manager  
Name & Address of the Office / Department: Piravom Municipality

To Vivekananda Public School  
Piravom  
(Name & Address of the Institution)

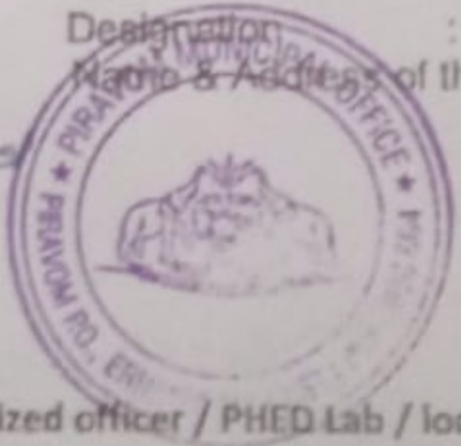

Note: The certificate is to be issued by authorized officer / PHED Lab / local bodies

Anump

VIVEKANANDA PUBLIC SCHOOL

Abhijith

MANAGER  
VIVEKANANDA PUBLIC SCHOOL  
PIRAVOM



Telephone: 0485-2997922  
email: qcsdlpiravom@gmail.com

**KERALA WATER AUTHORITY**  
**QUALITY CONTROL SUB DISTRICT LAB, PIRAVOM-686664**  
**WATER TEST-BACTERIOLOGY REPORT**

Report No: KWA/QCSDL-PVM/2133/25-26 Report Issue Date: 01.07.2025

Customer Name & Address  VIVEKANANDA PUBLIC SCHOOL PAZHOOR P.O PIRAVOM	Date of Receipt of Payment	24.06.25
	Date of Sample received	26.06.25
	Sample given by	Customer
	Sample Code	PVM/2133/06/25
	Sample Name	Drinking Water
	Sample Condition	Good
	Source of Sample	Open Well
	Sample Quantity	200ml
Test performing dates : From :27.06.25 to 28.06.25		

Sl. No.	Parameter	Acceptable Limit as per IS 10500-2012	Test Method	Result
1	Total Coliform	Shall not be Detected/100ml	IS15185-2016	Absent
2	E-Coli	Shall not be Detected/100ml	IS15185-2016	Absent

Remarks:-

- NB:-1) The result stated above related only to the sample(s) submitted for testing by the customer .  
2) The samples retain for 15 days from the end date of analysis  
3) The test certificate shall not be reproduced except in full without the written approval of the Laboratory

Authorized By



End of Report

VIDYALAKSHMI K G

KWA/QCSDL/PVM/F 21		Issue Date : 22.09.2021	
Rev No: 03	Rev Date : 11/02/2025	Page 1 of 1	

*Amey*  
PRINCIPAL  
VIVEKANANDA PUBLIC SCHOOL

*Baburaj*  
MANAGER  
VIVEKANANDA PUBLIC SCHOOL  
PIRAVOM



Telephone: 5485-297922  
 email: qc@piravom@gmail.com

## KERALA WATER AUTHORITY

QUALITY CONTROL SUB DISTRICT LAB, PIRAVOM -686664  
 (NABL RECOGNIZED LABORATORY)

### WATER TEST REPORT

Report No: KWA/QCSDL-PVM/2133/25-26	Date of Receipt of Payment	24.06.25
Customer Name & Address  VIVEKANANDA PUBLIC SCHOOL, PAZHOOOR P.O PIRAVOM	Date of Sample received	26.06.25
	Sample given by	Customer
	Sample Code	PVM/2133/06/25
	Sample Name	Drinking Water
	Sample Condition	Good
	Source of Sample	Open Well
	Sample Quantity	2 Litre
	Test performing dates :	From :24.06.25 to 27.06.25

Report Issue Date: 01.07.2025

SLN	Characteristics	Unit	Test Method	Acceptable Limit as per IS 10500-2012	Result
1	Turbidity	NTU	IS 3025 (Part10)-2023	1	0.37
2	pH at 25°C	-	IS 3025 (Part 11)-1983(Reaffirmed 2022)	6.5 to 8.5	5.90
3	Total Hardness (as CaCO <sub>3</sub> )	mg/L	IS 3025 (Part21)-2009(Reaffirmed 2019)	200	21.56
4	Chloride (as Cl)	mg/L	IS 3025 (Part 32)-1988(Reaffirmed 2019)	250	9.09
5	Electrical conductivity at 25°C	micromhos/cm	IS 3025 (Part 14)-2013(Reaffirmed 2019)	-	46.65
6	Iron (as Fe)	mg/L	IS 3025 (Part 53)-2024	1	BDL
7	Nitrate (as NO <sub>3</sub> )	mg/L	IS 3025 (Part 34/Sec.1) 2023	45	1.14

Remarks - DL : Detectable Limit  
 BDL : Below Detectable Limit

- NB -1) The result stated above related only to the sample(s) submitted for testing by the customer  
 2) The samples retain for 15 days from the end date of analysis  
 3) The test certificate shall not be reproduced except in full without the written approval of the Laboratory



Analysed By: *[Signature]*  
 TECHNICAL MANAGER

End of Report

SHEENAMOL M S

KWA/QCSDL/PVM/F 21	Issue Date : 22.09.2021
Rev No: 03	Rev Date : 11/02/2025
	Page 1 of 1

*[Signature]*  
 PRINCIPAL  
 VIVEKANANDA PUBLIC SCHOOL

*[Signature]*  
 MANAGER  
 VIVEKANANDA PUBLIC SCHOOL  
 PIRAVOM
